

LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Final Submission Report

Student Name and SRN	Prateek Hachadad, PES1UG24CS340
Jira Project	My Software Team
Scenario	Micro-Lending & Peer Credit Risk Assessor
Sprint Period	September 8, 2026 - September 15, 2026
Assessment Evidence	Backlog, Story Points, 2 Sprints, Burndown Charts, Reflection

Assessment focus: converting Lab 1 requirements into Agile Epics and User Stories, prioritizing and estimating backlog items with Fibonacci Story Points, simulating two one-week sprints, and interpreting the Jira Sprint Burndown Chart.

1. Scenario and Assessment Overview

The project scenario is a peer-to-peer micro-finance platform that calculates borrower risk scores using heuristic rules, generates structured repayment schedules, and triggers automated default warnings. The target stakeholders are the Borrower and Peer Lender.

For Lab 2, these capabilities were organized into three functional Epics and eight User Stories. The backlog was prioritized, estimated using Fibonacci Story Points, and split across two simulated sprints.

Epic	Stories	Points
Borrower Risk Assessment	3	11
Loan & Repayment Management	3	16
Default Monitoring & Alerts	2	10
Total	8	37

Key Agile conventions applied

User Stories use the required 'As a user role, I want a goal, so that a benefit' structure. Priorities were assigned as High or Medium according to user impact. Story Points use the Fibonacci sequence and represent relative effort, complexity, risk, and uncertainty rather than hours.

2. Jira Backlog - Epics, User Stories, Priorities and StoryPoints

The final backlog was organized under three Epics. High-priority core functions were placed ahead of the medium-priority secondary function.

Epic	User Story	Priority	Points
Borrower Risk Assessment	Calculate Borrower Credit Risk	High	5
	Display Risk Rating	High	3
	Validate Borrower Financial Profile	High	3
Loan & Repayment Management	Generate Repayment Schedule	High	5
	Process EMI Distribution	High	8
	View Repayment Status	Medium	3
Default Monitoring & Alerts	Monitor Repayment Behaviour	High	5
	Trigger Default Warning	High	5

Jira backlog evidence (final planning view):

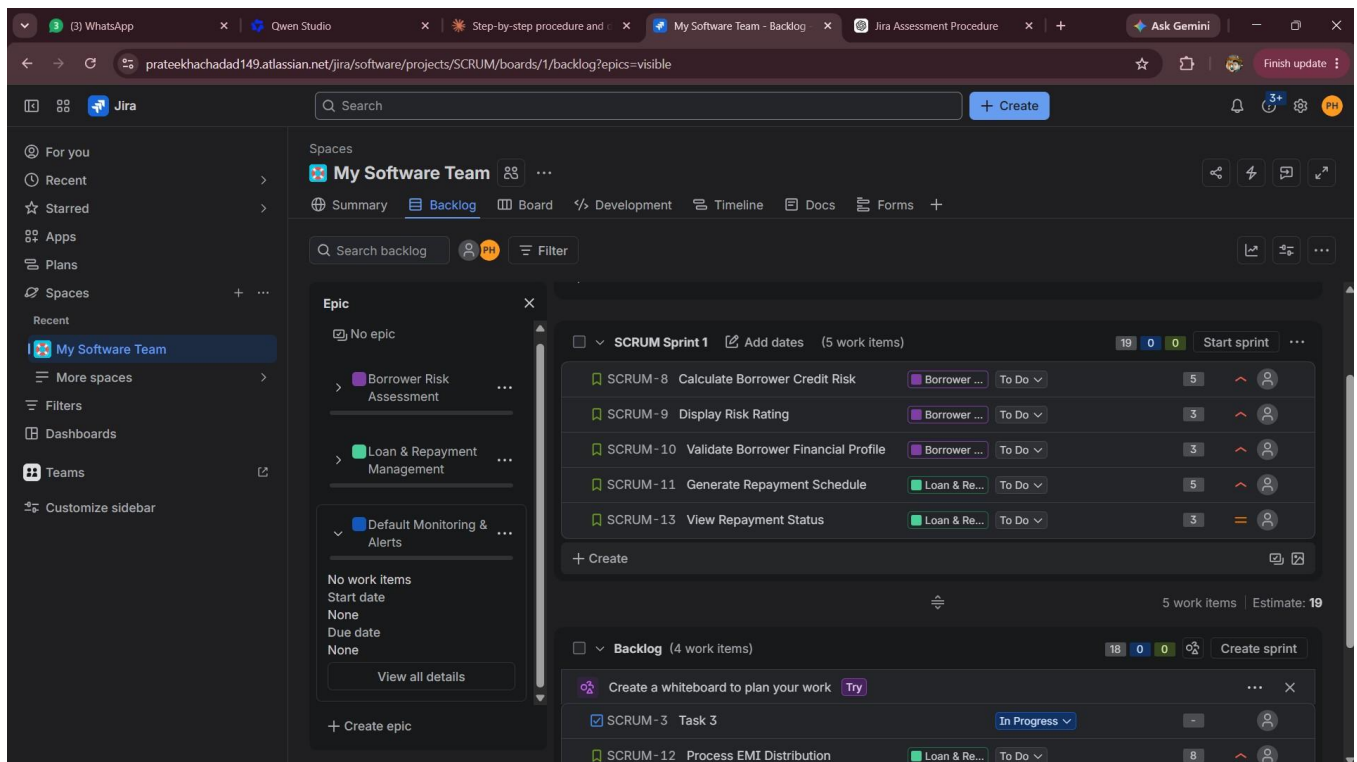


Figure 1. Jira backlog showing Sprint 1 planning, the five selected Stories, their Epic relationships, and Story Point estimates.

3. Sprint 1 Execution

Sprint 1 was planned as a one-week sprint from September 8 to September 15, 2026. Five prioritized Stories totaling 19 Story Points were selected. The sprint was simulated by moving the Stories through To Do, In Progress, and Done.

Sprint 1 Story	Points
Calculate Borrower Credit Risk	5
Display Risk Rating	3
Validate Borrower Financial Profile	3
Generate Repayment Schedule	5
View Repayment Status	3
Total	19

Sprint 1 completed board:

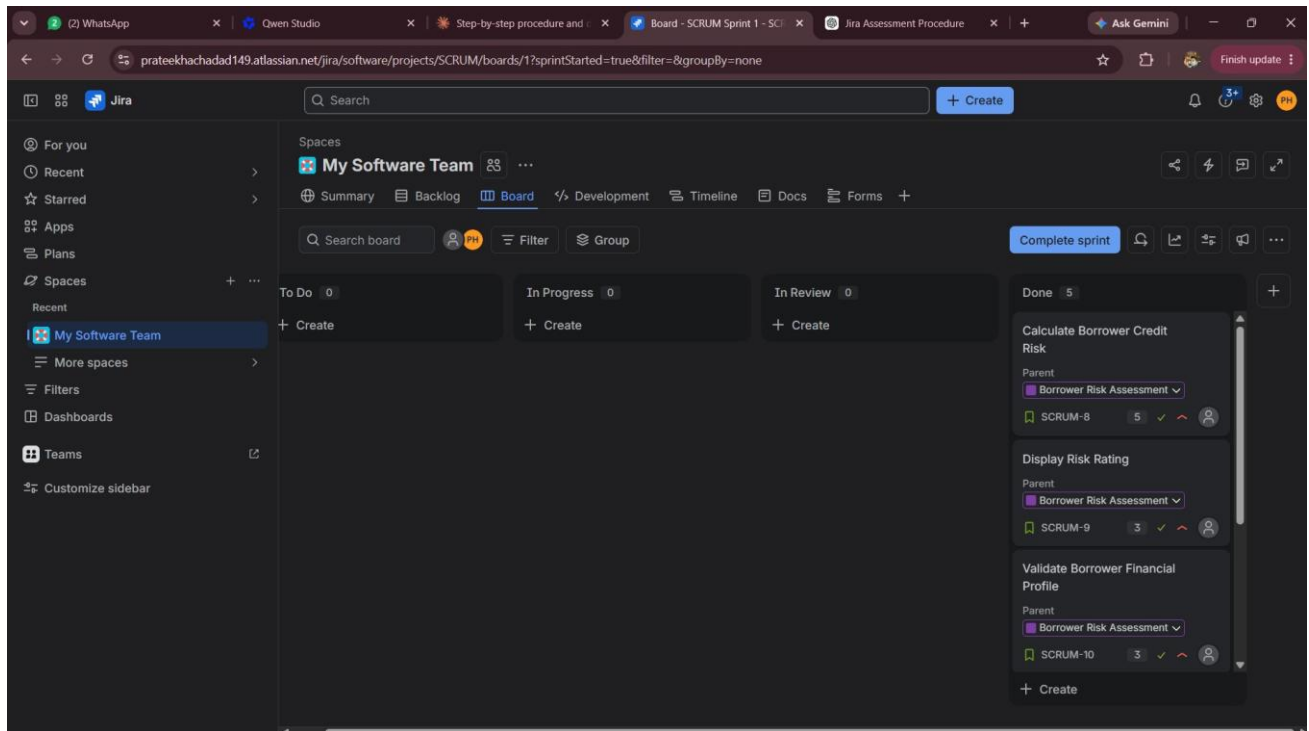


Figure 2. Jira Active Sprint board after all five Sprint 1 Stories were moved to Done.

4. Sprint 2 Execution

Sprint 2 used the remaining three assessment Stories for a planned total of 18 Story Points. The same one-week time box (September 8-15, 2026) was used for the classroom simulation.

Sprint 2 Story	Points
Process EMI Distribution	8
Monitor Repayment Behaviour	5
Trigger Default Warning	5
Total	18

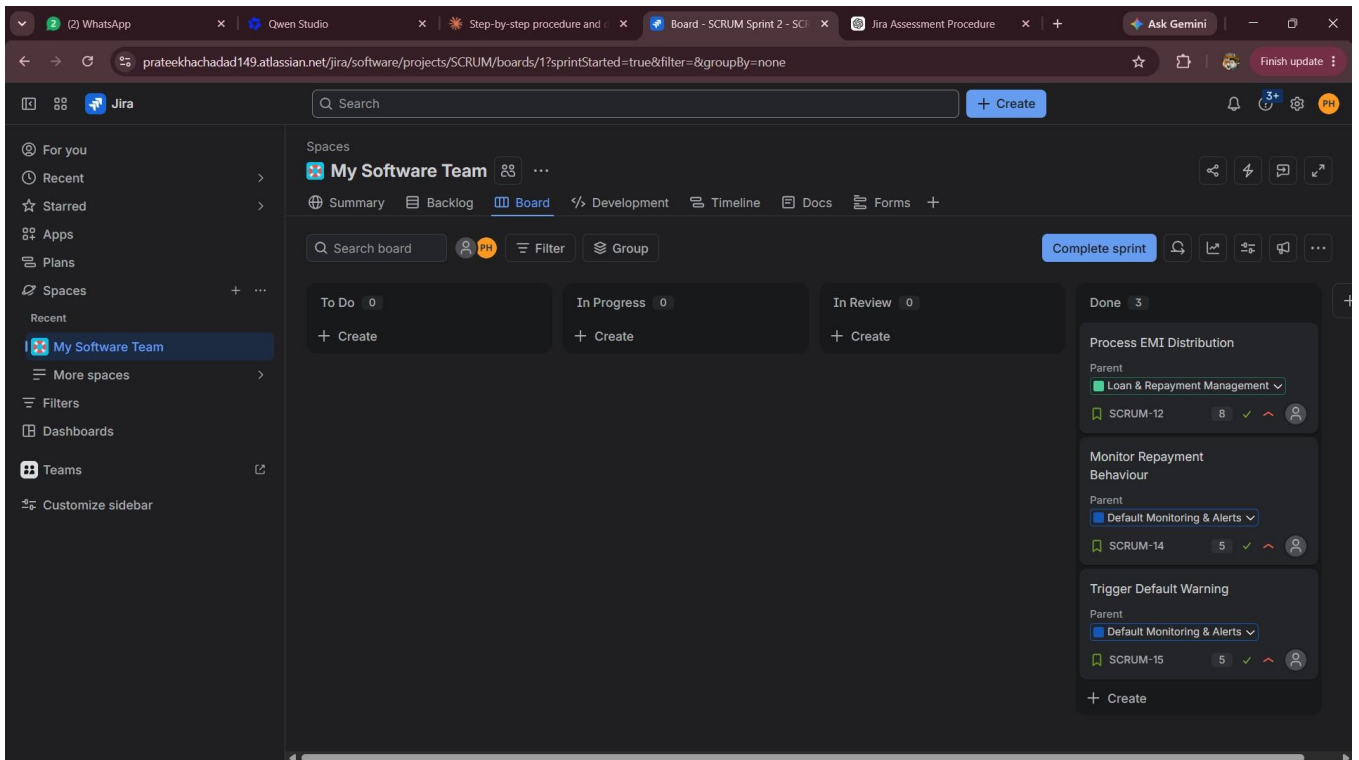


Figure 3. Jira Active Sprint board showing the three Sprint 2 Stories completed in Done.

5. Sprint 1 Burndown Chart

The Jira Sprint Burndown Chart was configured with Story points as the estimation field. The red line represents remaining work and the grey line is the ideal burn guideline.

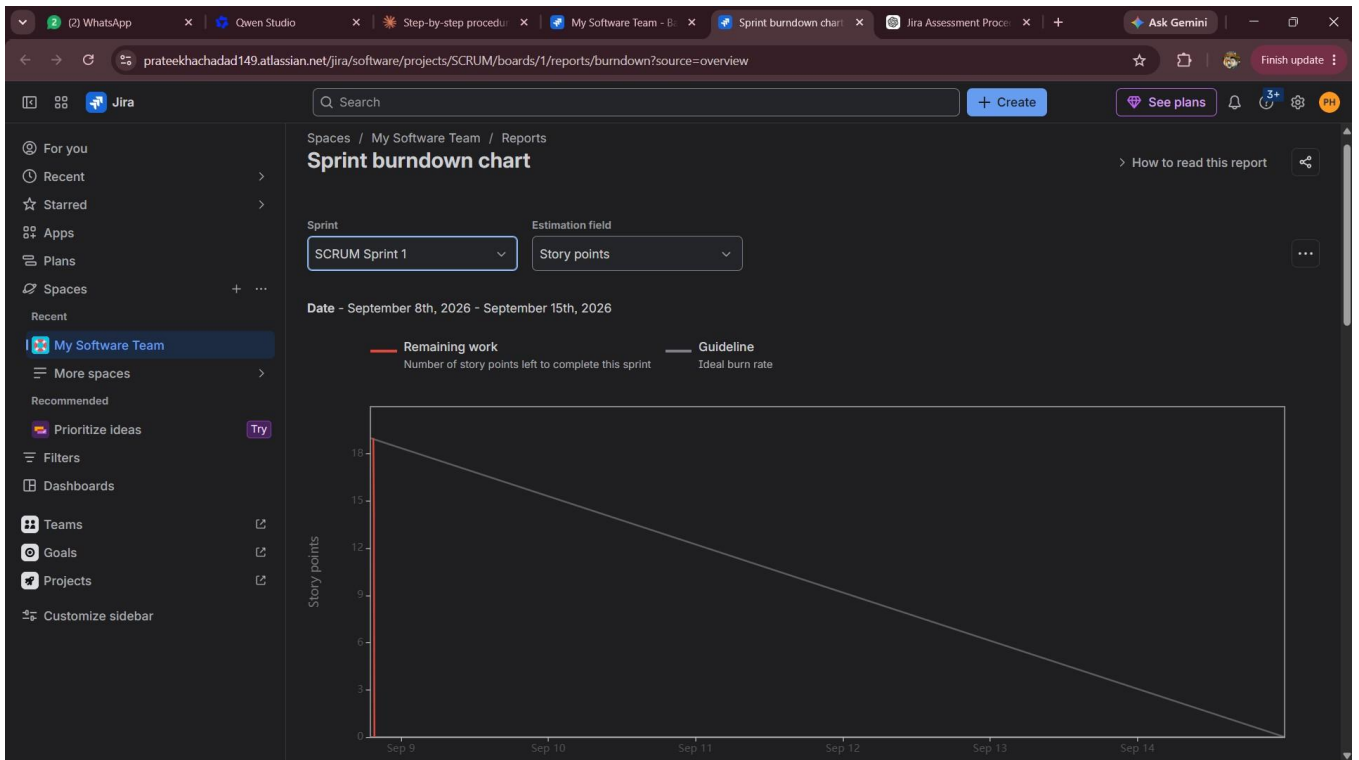


Figure 4. Jira-generated Sprint 1 Burndown Chart. The simulation completed the planned 19 Story Points on the same day the sprint was started, so the remaining-work line drops sharply to zero.

Observation

The chart confirms that the Sprint 1 workload was completed within the configured sprint window. Because the lab was performed as a same-day simulation, the chart does not represent a normal seven-day distribution of effort; instead, it records the actual Jira status changes made during the exercise.

6. Sprint 2 Burndown Chart

The same Jira Burndown report was used for Sprint 2 with Story points as the estimation statistic.

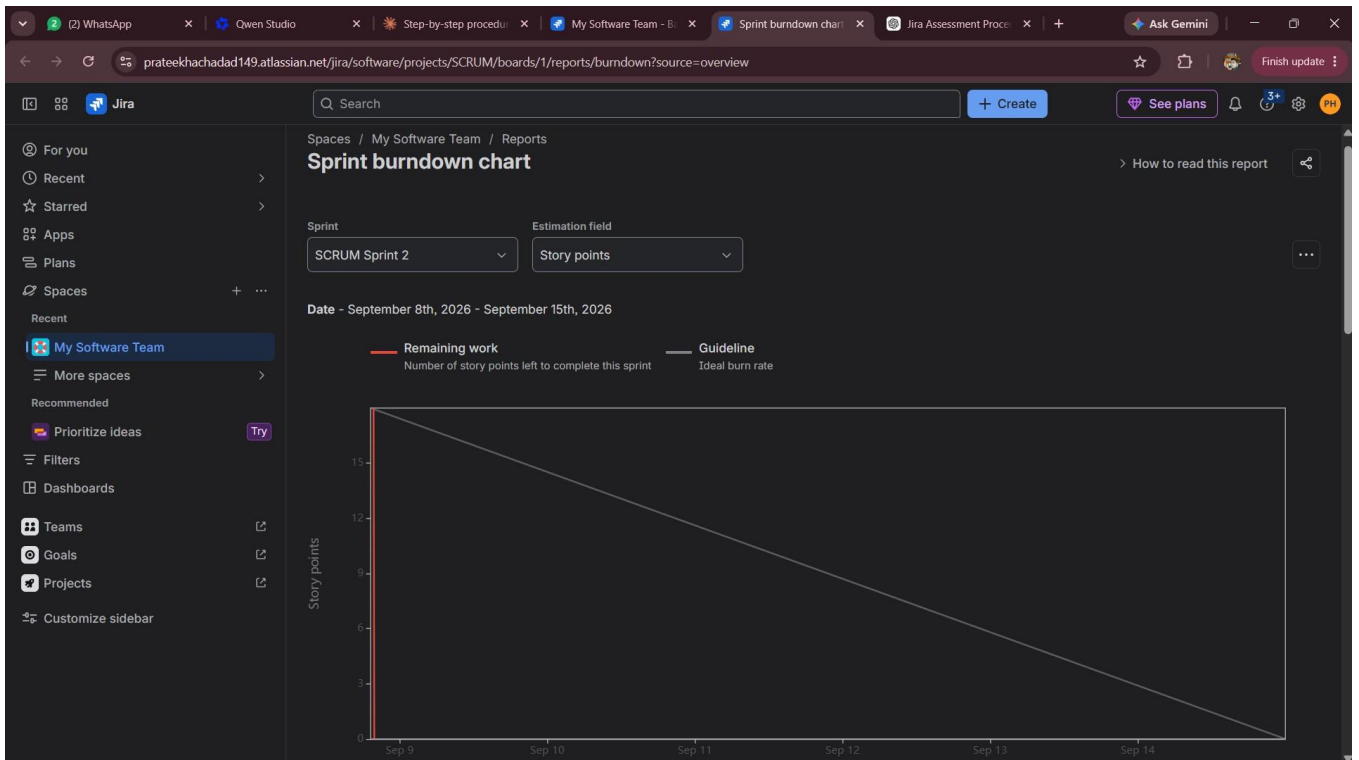


Figure 5. Jira-generated Sprint 2 Burndown Chart. The remaining 18 Story Points are shown reaching zero after the simulated completion of all three Stories.

Observation

Sprint 2 also finished all planned work within the configured time box. The chart provides a direct visual record of remaining Story Points and the ideal burn guideline, which is the intended use of the Burndown report.

7. Reflection

1. Did your estimations reflect the actual effort?

The estimates were reasonable as relative measures of difficulty. The 8-point Process EMI Distribution story was treated as the most complex item, while smaller stories were estimated at 3 or 5 points. The simulated execution completed all planned Stories, so the estimates were adequate for the exercise, although the same-day simulation does not provide a realistic measure of elapsed development effort.

2. Was your backlog well-prioritized?

Yes. Core credit assessment and repayment functions were assigned High priority, while the secondary View Repayment Status story was assigned Medium priority. The resulting backlog placed the most important functionality ahead of the lower-impact item.

3. How did your simulated sprint align with your plan?

Sprint 1 completed the planned 19 Story Points across five Stories, and Sprint 2 completed the remaining 18 Story Points across three Stories. Both sprints followed the planned workflow of To Do to In Progress to Done and stayed within the configured one-week sprint window.

4. What insights did the burndown chart give about your team's capacity?

The exercise demonstrated that the team could complete 19 Story Points in Sprint 1 and 18 Story Points in Sprint 2 in the simulation. The Burndown Charts also showed that work was completed faster than the ideal guideline because all items were closed on the same day. This indicates that the observed capacity is a simulation result rather than a production-ready velocity forecast.

8. Submission Evidence Checklist

Required evidence	Included
Epics and User Stories	Yes
Priority assignments	Yes
Story Point assignments	Yes
Sprint 1 Active Sprint	Yes
Sprint 2 Active Sprint	Yes
Sprint 1 Burndown Chart	Yes
Sprint 2 Burndown Chart	Yes
Four reflection questions	Yes
